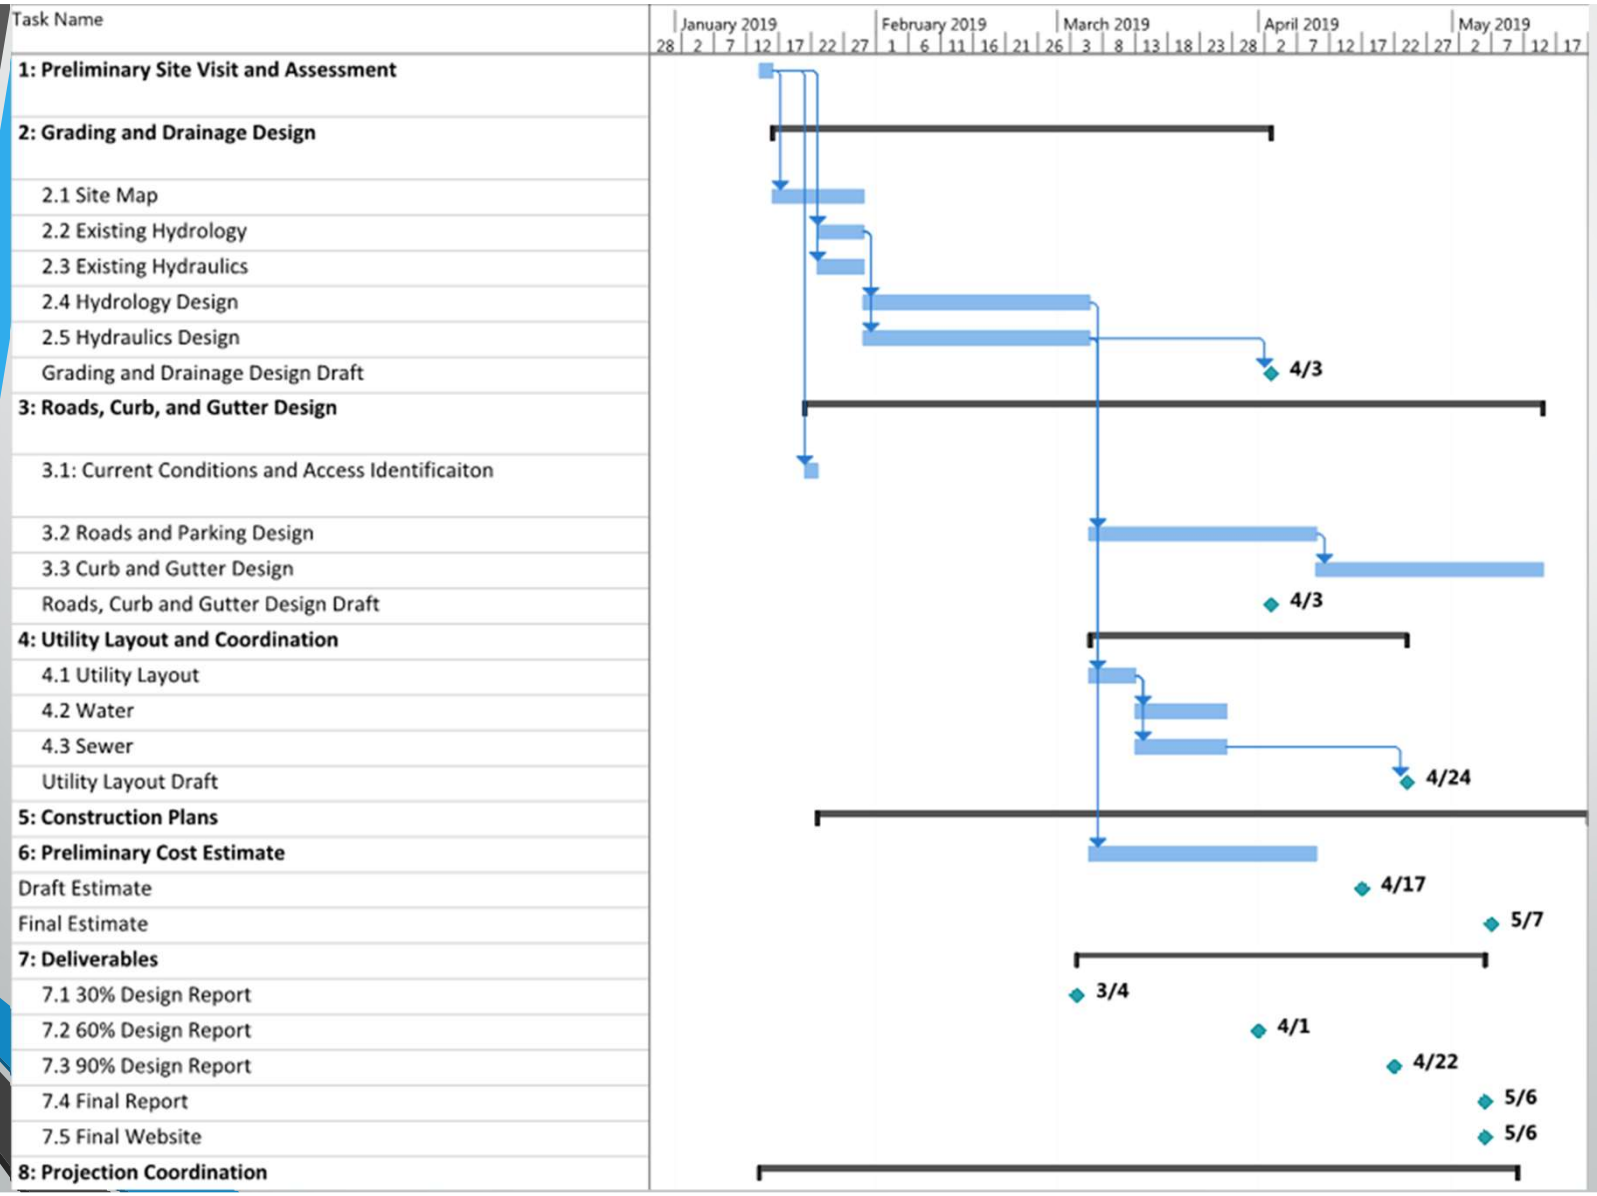
Task Name
January 2019
February 2019
March 2019
April 2019
May 2019
28 2 7 12 17 22 27 1 6 11 16 21 26 3 8 13 18 23 28 2 7 12 17 22 27 2 7 12 17
1: Preliminary Site Visit and Assessment
2: Grading and Drainage Design
2.1 Site Map
2.2 Existing Hydrology
2.3 Existing Hydraulics
2.4 Hydrology Design
2.5 Hydraulics Design
Grading and Drainage Design Draft
4/3
3: Roads, Curb, and Gutter Design
3.1: Current Conditions and Access Identificaiton
3.2 Roads and Parking Design
3.3 Curb and Gutter Design
Roads, Curb and Gutter Design Draft
4/3
4: Utility Layout and Coordination
4.1 Utility Layout
4.2 Water
4.3 Sewer
Utility Layout Draft
4/24
5: Construction Plans
6: Preliminary Cost Estimate
Draft Estimate
4/17
Final Estimate
5/7
7: Deliverables
7.1 30% Design Report
3/4
7.2 60% Design Report
4/1
7.3 90% Design Report
4/22
7.4 Final Report
5/6
7.5 Final Website
5/6
8: Projection Coordination
