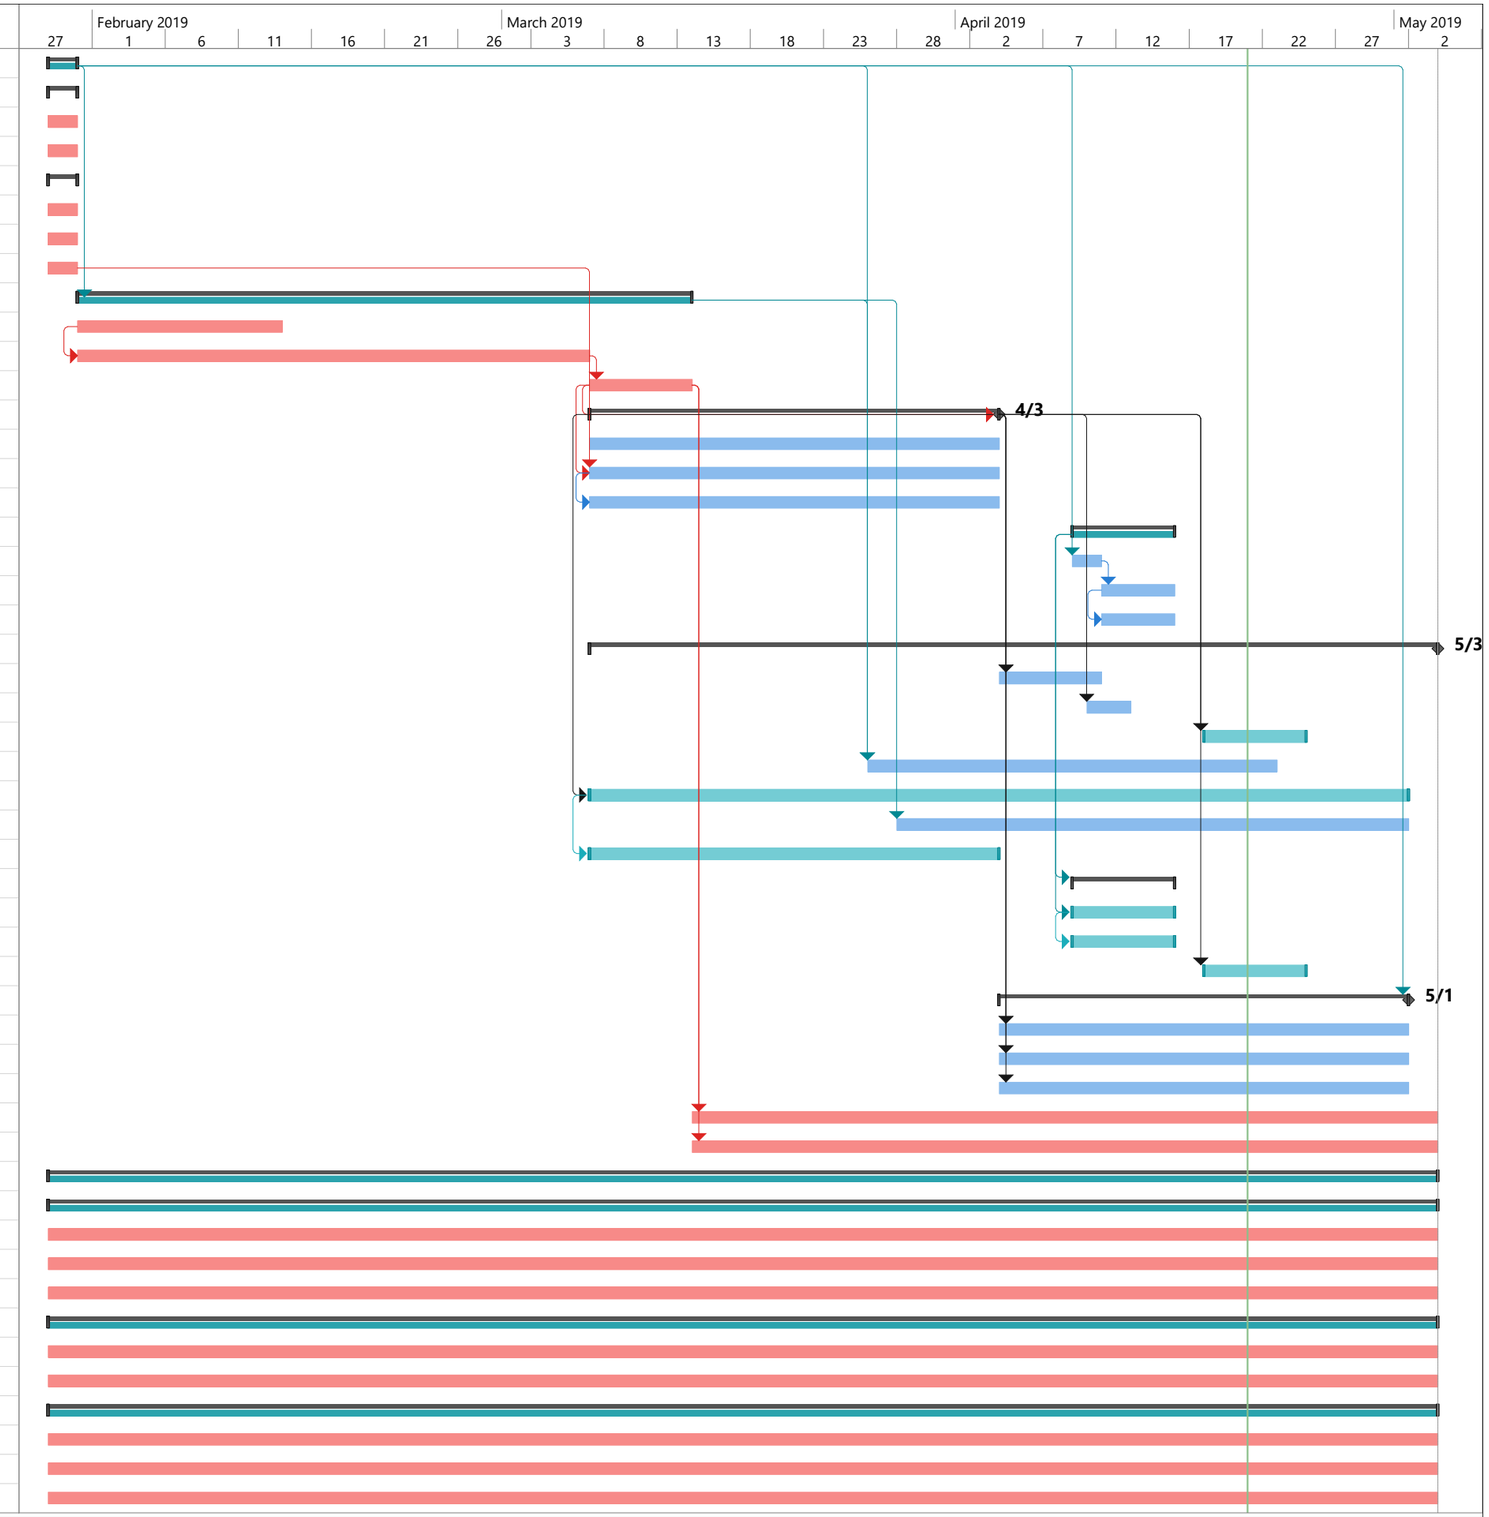ID	Task Name	Duration	Start	Finish
1	1 Site Assessment	2 days	Tue 1/29/19	Wed 1/30/19
2	1.1 Road Condition Assessment	2 days	Tue 1/29/19	Wed 1/30/19
3	1.1.1 Asphalt Condition	2 days	Tue 1/29/19	Wed 1/30/19
4	1.1.2 Shoulder Condition	2 days	Tue 1/29/19	Wed 1/30/19
5	1.2 Drainage Condition Assessment	2 days	Tue 1/29/19	Wed 1/30/19
6	1.2.1 Culvert Condition and Location	2 days	Tue 1/29/19	Wed 1/30/19
7	1.2.2 Wash Integrity	2 days	Tue 1/29/19	Wed 1/30/19
8	1.3 Right of Way Assessment	2 days	Tue 1/29/19	Wed 1/30/19
9	2 Hydrology and Hydraulics Analysis	30 days	Thu 1/31/19	Wed 3/13/19
10	2.1 Map Culverts	10 days	Thu 1/31/19	Wed 2/13/19
11	2.2 Hydrology	25 days	Thu 1/31/19	Wed 3/6/19
12	2.3 Hydraulics	5 days	Thu 3/7/19	Wed 3/13/19
13	3 Highway Design	20 days	Thu 3/7/19	Wed 4/3/19
14	3.1 Cross Sections	20 days	Thu 3/7/19	Wed 4/3/19
15	3.2 Plan View	20 days	Thu 3/7/19	Wed 4/3/19
16	3.3 Profile View	20 days	Thu 3/7/19	Wed 4/3/19
17	4 Traffic Control Plan	5 days	Tue 4/9/19	Mon 4/15/19
18	4.1 Phasing	2 days	Tue 4/9/19	Wed 4/10/19
19	4.2 Quantities	3 days	Thu 4/11/19	Mon 4/15/19
20	4.3 Duration	3 days	Thu 4/11/19	Mon 4/15/19
21	5 Design Plan Sets	42 days	Thu 3/7/19	Fri 5/3/19
22	5.1 Face Sheet	5 days	Thu 4/4/19	Wed 4/10/19
23	5.2 Typical Roadway Sections Sheet	3 days	Wed 4/10/19	Fri 4/12/19
24	5.3 Geometric Control Sheet	5 days	Thu 4/18/19	Wed 4/24/19
25	5.4 Existing Conditions and Removal Sheet	20 days	Tue 3/26/19	Mon 4/22/19
26	5.5 Roadway Plan and Profile Sheets	40 days	Thu 3/7/19	Wed 5/1/19
27	5.6 Drainage Plans and Details Sheets	25 days	Thu 3/28/19	Wed 5/1/19
28	5.7 Intersection Plans and Details	20 days	Thu 3/7/19	Wed 4/3/19
29	5.8 Traffic Control Plan Sheets	5 days	Tue 4/9/19	Mon 4/15/19
30	5.8.1 Sequence of Construction Sheet	5 days	Tue 4/9/19	Mon 4/15/19
31	5.8.2 Traffic Control Durations and Quantities Sheet	5 days	Tue 4/9/19	Mon 4/15/19
32	5.9 Roadway Cross Section Sheets	5 days	Thu 4/18/19	Wed 4/24/19
33	5.10 Cost Estimate Report Sheet	20 days	Thu 4/4/19	Wed 5/1/19
34	5.10.3.1 Site Obstruction Removal	20 days	Thu 4/4/19	Wed 5/1/19
35	5.10.3.2 Excavation, Backfill, Embankment	20 days	Thu 4/4/19	Wed 5/1/19
36	5.10.3.3 Construction	20 days	Thu 4/4/19	Wed 5/1/19
37	5.11 Drainage Report- Roadway	37 days	Thu 3/14/19	Fri 5/3/19
38	5.12 Drainage Report- Structures	37 days	Thu 3/14/19	Fri 5/3/19
39	6 Project Management	69 days	Tue 1/29/19	Fri 5/3/19
40	**6.1 Project Meetings**	**69 days**	**Tue 1/29/19**	**Fri 5/3/19**
41	6.1.1 Client Meetings	69 days	Tue 1/29/19	Fri 5/3/19
42	6.1.2 Team Meetings	69 days	Tue 1/29/19	Fri 5/3/19
43	6.2 Deliverables	69 days	Tue 1/29/19	Fri 5/3/19
44	**6.3 Documentation**	**69 days**	**Tue 1/29/19**	**Fri 5/3/19**
45	6.3.1 Meetings	69 days	Tue 1/29/19	Fri 5/3/19
46	6.3.2 Hours	69 days	Tue 1/29/19	Fri 5/3/19
47	**6.4 Manage Resources**	**69 days**	**Tue 1/29/19**	**Fri 5/3/19**
48	6.4.1 Equipment	69 days	Tue 1/29/19	Fri 5/3/19
49	6.4.2 Materials	69 days	Tue 1/29/19	Fri 5/3/19
50	6.4.3 Transportation	69 days	Tue 1/29/19	Fri 5/3/19
